Consolidated Communications Update

NASDAQ: CNSL | www.consolidated.com

Agenda

- Introduction
- What we've been up to
- What it means to Lancaster
- Q & A

What we're bringing to Lancaster

$40M ARPA Grant Towns-2024 Construction Rollout

Wire Center	Town(s)	Construction Start	Construction Complete	Construction Complete Year	Grant Passings (24,757)	Total Passings	Miles	Fiber Placement	Splicing	Testing	Ready for Installs
Alstead	Alstead, Acworth	15-Feb	8-Apr	2024	568	1,566	78	100%	100%	100%	Yes
Berlin	Berlin	2-Jan	15-Apr	2024	1,368	6,244	76	100%	100%	100%	Yes
Gorham	Gorham, Randolph, Shelburne	2-Jan	22-Apr	2024	534	2,134	65	100%	100%	100%	Yes
Moultonborough	Moultonborough	15-Feb	6-May	2024	218	1,558	47	100%	100%	100%	Yes
Winchester	Winchester, Richmond	15-Feb	1-Jul	2024	2,659	2,788	116	100%	100%	100%	Yes
Center Harbor	Center Harbor, Moultonborough	15-Feb	8-Jul	2024	338	5,624	126	100%	100%	100%	Yes
Littleton	Littleton	1-Apr	22-Jul	2024	1,259	5,069	141	100%	100%	100%	Yes
Hancock	Hancock	6-May	29-Jul	2024	280	1,062	57	100%	100%	100%	Yes
Madison	Madison	6-May	30-Jul	2024	616	1,979	82	100%	100%	100%	Yes
Sunapee	Sunapee, Newbury, New London	22-May	11-Oct	2024	2,653	4,142	131	100%	100%	100%	Yes
Milan	Milan, Dummer	1-May	15-Oct	2024	1,253	1,253	74	100%	100%	100%	Yes
Errol	Errol	15-Mar	28-Oct	2024	701	874	47	100%	100%	100%	Yes
Hinsdale	Hinsdale, Winchester	23-Sep	11-Nov	2024	195	610	23	100%	95%	95%	No
Groveton	Groveton, Northumberland, Stark, Stratford	6-May	18-Nov	2024	947	2,311	100	100%	100%	78%	No
Whitefield	Whitefield, Dalton	15-Jul	18-Nov	2024	1,457	2,485	94	98%	88%	0%	No
Pittsburg	Pittsburg	28-May	25-Nov	2024	1,591	2,347	83	100%	99%	63%	No
Bethlehem	Bethlehem	31-Jul	25-Nov	2024	451	1,467	55	100%	90%	40%	No
Jefferson	Jefferson	21-Oct	15-Feb	2025	504	755	TBD	0%	0%	0%	No
Bartlett	Bartlett	21-Oct	15-Feb	2025	714	714	TBD	0%	0%	0%	No
Center Ossipee	Ossipee, Effingham, Tuftonboro, and Freedom	21-Oct	15-Mar	2025	3,538	8,807	TBD	20%	8%	0%	No
Tamworth	Tamworth	11-Nov	15-Mar	2025	1,256	2,266	TBD	0%	0%	0%	No
North Fryeburg	Chatham	Q1	15-Apr	2025	281	282	TBD	0%	0%	0%	No
Franconia	Franconia, Sugar Hill, Easton	Q1	15-May	2025	862	2,239	87	0%	0%	0%	No
Newport	Newport, Croydon	Q1	15-Jun	2025	607	607	TBD	0%	0%	0%	No
					17,088	43,513	1395	72%	70%	61%	

Construction Plans & Timing

We're in Phase 1:
Pre-construction Planning

Phase 2:
Fiber Construction

Start Q1 2024

Phase 3:
Splicing

2-3 Months

Phase 4:
Testing and
Pre-orders

1-2 Months

Phase 5: Ready for Sale

<u>Key Statistics for Lancaster Build</u>

- **Total Passings: 2,593 (395-Grant Addresses)**
- **Estimated Construction Start Month: Q1 2025**
- **Estimated Construction Completion Month: Q2 2025**

Working Together: Communication Cadence

Suggested Communications Plan

- Report with the following information:
  - Project updates/Progress
  - Issues/Concerns
  - Upcoming Events

- Conversations as needed:
  - Permit issues
  - Construction questions
  - Resident feedback

Sample of an Overview Map and the Report

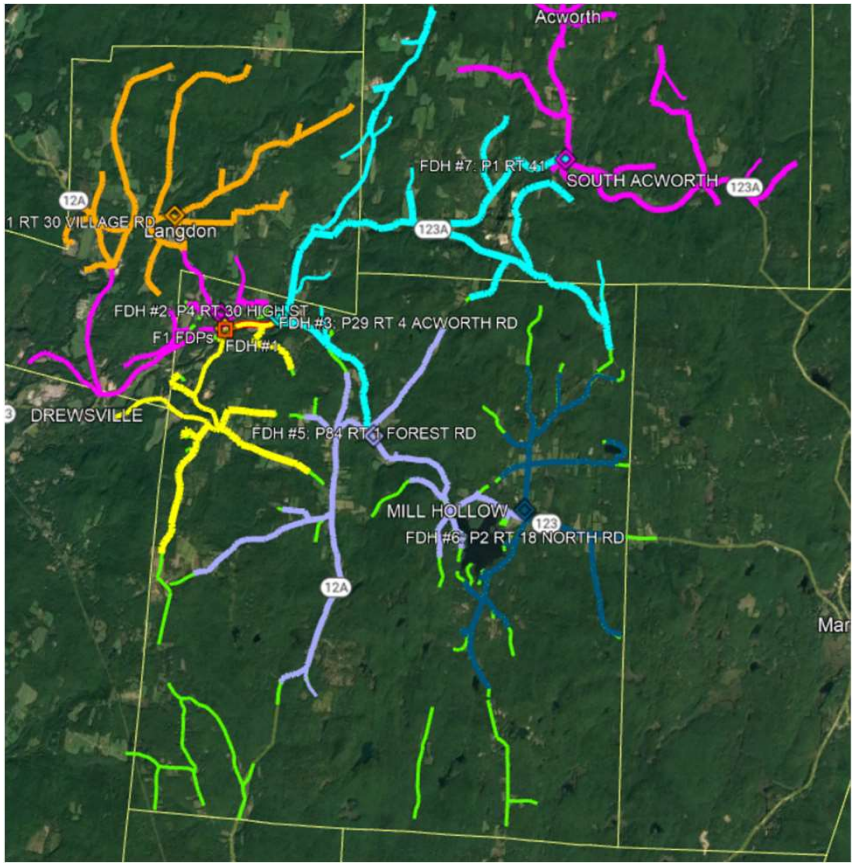

Job	Fiber Built %	Splicing %	Testing Complete	Install Status
FDH #1 "Yellow"	100%	100%	100%	Ready
FDH #2 " Light Pink" Rt 30 High St	100%	100%	100%	Ready
FDH #3 "Light Blue" RT 4 Acworth Rd	100%	100%	100%	Ready
FDH #5 "Light Purple" Rt 1 Forest Rd	100%	100%	100%	Ready
FDH #6 "Dark Teal" Rt 18 North Rd	100%	100%	100%	Ready
FDH #7 "Pink" RT 41 South Acworth	100%	100%	100%	Ready

Next Steps

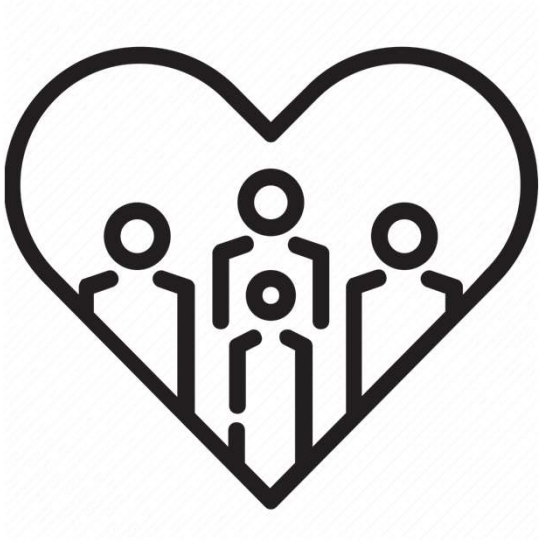

Connect with the community

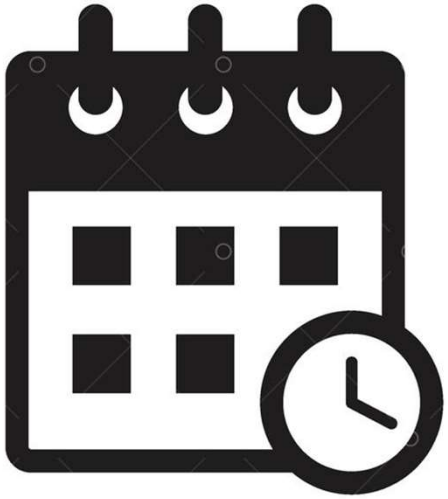

Schedule upcoming touchpoints

Questions? Call us.

CONFIDENTIAL AND PROPRIETARY – ONLY FOR INTERNAL USE
